SOUTHLAKE COMMERCIAL CONSTRUCTION MANAGEMENT, LLC

EYES FORT WORTH
3444 & 3450 HULEN
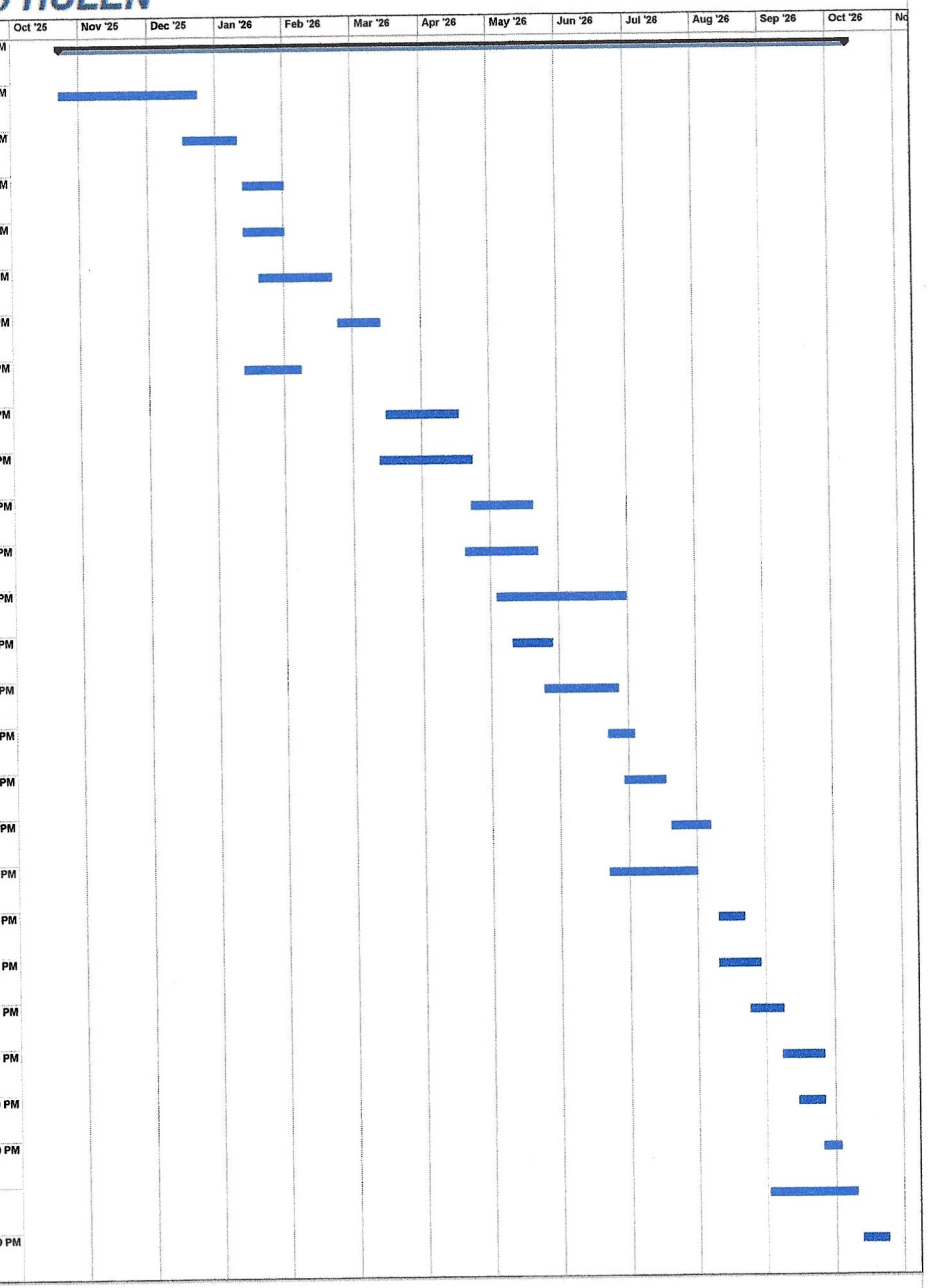
	Task Name	Duration	Start	Finish
1	*Eyes Fort Worth*	253 days?	Wed 10/22/25 8:00 AM	Fri 10/9/26 5:00 PM
2	Permitting & CFA Work	44 days	Wed 10/22/25 8:00 AM	Mon 12/22/25 5:00 PM
3	Excavation & building pad prep	19 days	Tue 12/16/25 8:00 AM	Fri 1/9/26 5:00 PM
4	Underground utilities to buildings	15 days	Mon 1/12/26 8:00 AM	Fri 1/30/26 5:00 PM
5	Layout building pads/drill and pour piers	15 days	Mon 1/12/26 8:00 AM	Fri 1/30/26 5:00 PM
6	Underground plumbing for buildings/dig grade beams	25 days	Mon 1/19/26 8:00 AM	Fri 2/20/26 5:00 PM
7	Pour building slabs	15 days	Mon 2/23/26 8:00 AM	Fri 3/13/26 5:00 PM
8	Install site conduits for communication, electrical & irrigation	20 days	Mon 1/12/26 8:00 AM	Fri 2/6/26 5:00 PM
9	Pour site paving for parking	25 days	Mon 3/16/26 8:00 AM	Fri 4/17/26 5:00 PM
10	Install structural steel & frame shell buildings	30 days	Fri 3/13/26 8:00 AM	Thu 4/23/26 5:00 PM
11	Roofing	20 days	Thu 4/23/26 8:00 AM	Wed 5/20/26 5:00 PM
12	Storefront/ exterior doors/windows, glass and glazing	25 days	Mon 4/20/26 8:00 AM	Fri 5/22/26 5:00 PM
13	Stucco	42 days	Mon 5/4/26 8:00 AM	Tue 6/30/26 5:00 PM
14	Interior stud framing for finish out	14 days	Mon 5/11/26 8:00 AM	Thu 5/28/26 5:00 PM
15	HVAC, electrical & plumbing rough in for walls & ceilings	25 days	Mon 5/25/26 8:00 AM	Fri 6/26/26 5:00 PM
16	Exterior shell building insulation	10 days	Mon 6/22/26 8:00 AM	Fri 7/3/26 5:00 PM
17	Sheetrock interior finish out	15 days	Mon 6/29/26 8:00 AM	Fri 7/17/26 5:00 PM
18	Tape,bed, texture and prime paint	14 days	Mon 7/20/26 8:00 AM	Thu 8/6/26 5:00 PM
19	Install all building sidewalks	30 days	Mon 6/22/26 8:00 AM	Fri 7/31/26 5:00 PM
20	Set acoustical ceiling grid	10 days	Mon 8/10/26 8:00 AM	Fri 8/21/26 5:00 PM
21	Interior door frames and doors	15 days	Mon 8/10/26 8:00 AM	Fri 8/28/26 5:00 PM
22	Install interior cabinets and millwork	11 days	Mon 8/24/26 8:00 AM	Mon 9/7/26 5:00 PM
23	2nd coat of paint and interior finishes - floor, base tile, etc	15 days	Mon 9/7/26 8:00 AM	Fri 9/25/26 5:00 PM
24	HVAC and electrical trim out	10 days	Mon 9/14/26 8:00 AM	Fri 9/25/26 5:00 PM
25	Set acoustical tile	5 days	Fri 9/25/26 8:00 AM	Fri 10/2/26 5:00 PM
26	Irrigation, landscape, fences guardrails/handrails, etc.	29 days	Tue 9/1/26 8:00 AM	Fri 10/9/26 5:00 PM
27	Final inspections -punch list	10 days	Mon 10/12/26 8:00 AM	Fri 10/23/26 5:00 PM
